

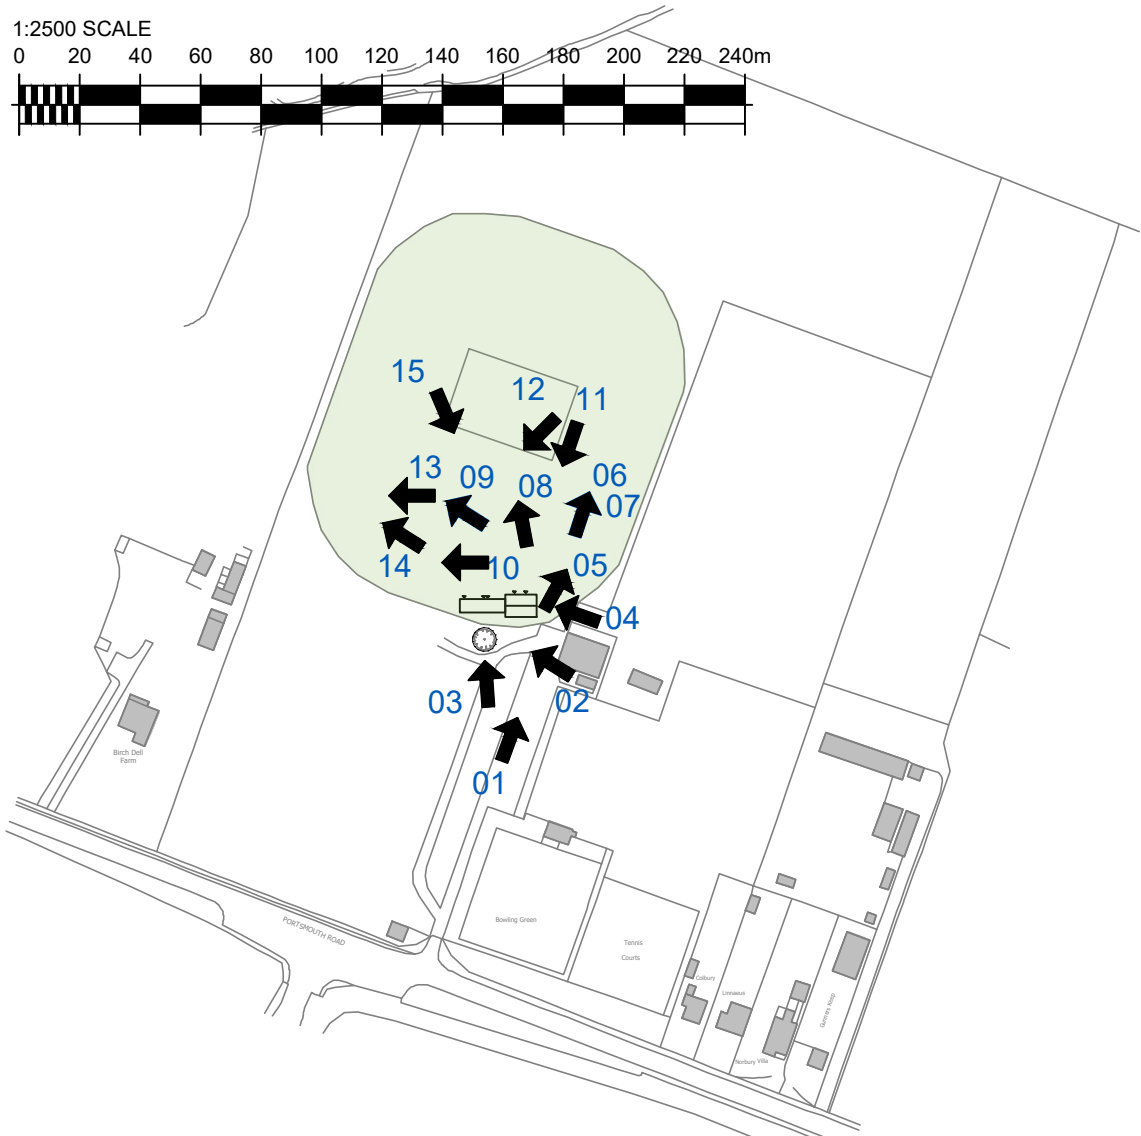



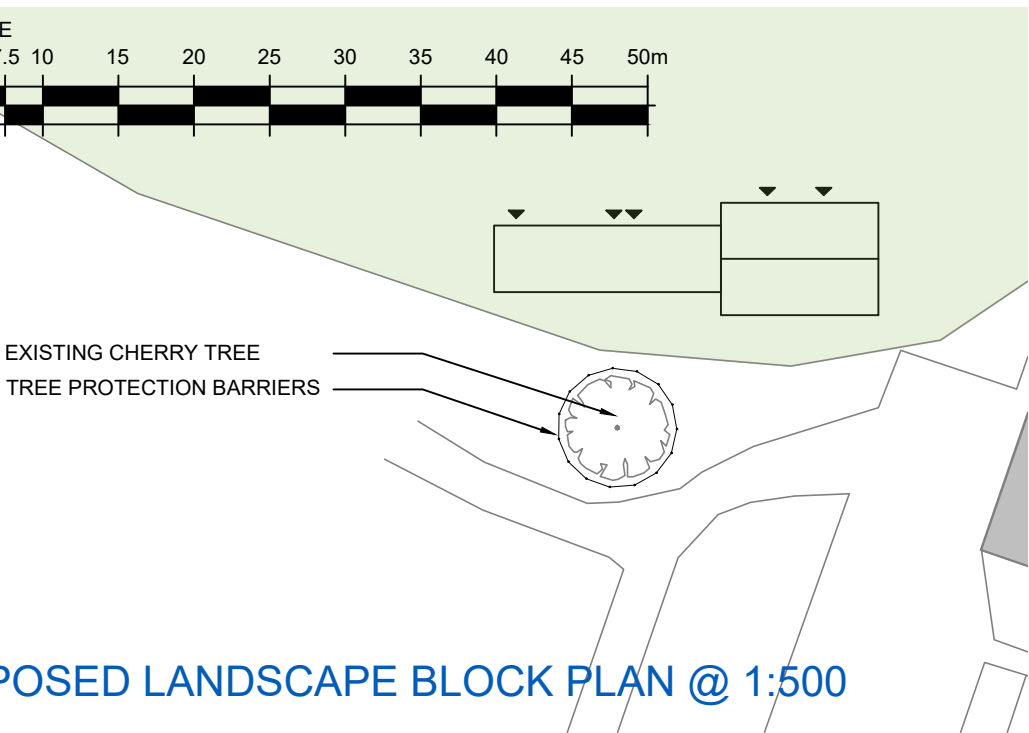

PROPOSED LANDSCAPE PLAN @ 1:2500




PROPOSED LANDSCAPE BLOCK PLAN @ 1:500

Tree Protection Plan & Arboricultural Method Statement.

- 1.1 Appointment of the Responsible Person.
  - 1.1.1 Before any site works, including site clearance, take place, a person will be made responsible for the correct and full implementation of this plan and statement (the Responsible Person). The Responsible Person will typically be the project manager or site manager, but whoever is appointed they will be deemed responsible for the full and correct implementation of this plan and statement, and will be deemed liable for any failure to correctly and fully implement this plan and statement.
  - 1.1.2 When appointed, the Responsible Person will inform the Local Planning Authority and the project of their appointment and will supply a full set of contact details.
- 1.2 Agreement of the arboricultural monitoring timetable.
  - 1.2.1 If specifically requested by the Local Planning Authority, before any site works, including site clearance, take place, a site meeting will be held with the Responsible Person, the site/project manager, and the Local Planning Authority's Tree Officer. The purpose of this meeting will be to confirm the tree protection measures required and a timetable of ongoing site monitoring and reporting.
  - 1.2.2 Further arboricultural monitoring and reporting will be carried out by the site/project manager in accordance with the timetable agreed at the above meeting.
- 1.3 Distribution of the Tree Protection Plan & Arboricultural Method Statement drawing.
  - 1.3.1 It is the responsibility of the Responsible Person to ensure that all staff and contractors working on the development are aware of and abide by this Tree Protection Plan & Arboricultural Method Statement.
  - 1.3.2 It is the responsibility of the Responsible Person to ensure that a scale copy of this drawing will be attached to the site office notice board, and that copies of this drawing will always be available for taking out on site as necessary.
  - 1.3.3 It is the responsibility of the Responsible Person to ensure that reference to this Tree Protection Plan & Arboricultural Method Statement forms part of the standard induction briefing for all personnel coming onto site.
- 1.4 General measures, including access, storage of materials etc.
  - 1.4.1 The following measures and restrictions will apply at all times.
  - 1.4.2 Before any construction works commence and before any construction equipment, vehicles and materials are delivered to site, with the exception of those necessary for the installation of tree protection barriers, the tree protection barriers should be erected in place if required.
  - 1.4.3 All construction traffic access will be via the existing access track off Portsmouth Road A3025.
  - 1.4.4 When any large and/or tall and/or jibbed vehicles/equipment are operating or maneuvering close to the crowns of trees to be retained, a specific banksperson will be appointed to supervise the movement and ensure that no damage is caused to the crowns of these trees through impact.
  - 1.4.5 All construction traffic parking will be in the existing car park.
  - 1.4.6 No fires will be permitted on site.
- 1.5 Tree Works.
  - 1.5.1 There are no specific tree works taking place
  - 1.5.2 All tree works will be carried out in accordance with the following stipulations.
    - 1.5.2.1 All tree works will be carried out in accordance with BS3998:2010 wherever that Standard is applicable.
    - 1.5.2.2 All works will be carried out in accordance with all applicable health & safety and environmental protection legislation.
    - 1.5.2.3 All tree works will be carried out in such a way that no unintended collateral harm is caused to trees to be retained.
- 1.6 Tree protection barrier erection
  - 1.6.1 Before any construction works commence, and before any construction vehicles, equipment and materials, other than only those necessary for the erection of the tree protection barriers, are delivered to site, the tree protection barriers will be erected at the positions illustrated in this drawing.
  - 1.6.2 This barrier will comprise a minimum 1 metre tall plastic barricade mesh fence, supported at no longer intervals than 2 metres, and close where the barrier needs to follow a curved line, and at every corner, on a minimum 1.5 metres tall road pin.
  - 1.6.3 The barrier will have an A3 size informative/warning notice attached to the top edge at no more than 6 metre intervals. Please refer to example of a suitable notice provided below.
  - 1.6.4 No construction access whatsoever will be permitted in the construction exclusion zones formed by the tree protection barriers.
  - 1.6.5 The tree protection barriers will be retained in place and intact until the proposed works have been completed and all construction materials, spoil, machinery, equipment and vehicles have been removed from site.



MATERIAL LEGEND



LEASE AGREEMENT AREA OF SITE FOR CRICKET CLUB. NO CONTROL OR INFLUENCE OUTSIDE OF THIS ZONE


Notes:

THIS DRAWING IS THE COPYRIGHT OF THE DESIGNER AND MAY NOT BE COPIED, ALTERED OR REPRODUCED IN ANY FORM, OR PASSED TO A THIRD PARTY WITHOUT THE WRITTEN CONSENT OF THE DESIGNER.

DIMENSIONS SHOULD BE CHECKED AND VERIFIED ON SITE AND ANY DISCREPANCIES SHOULD BE REPORTED TO THE DESIGNER.

DO NOT SCALE FROM THIS DRAWING, EXCEPT FOR PLANNING PURPOSES. USE FIGURED DIMENSIONS ONLY.

IF IN DOUBT ASK FOR CONFIRMATION.



|         |                                    |          |          |
|---------|------------------------------------|----------|----------|
| A       | TREE PROTECTION BARRIERS INDICATED | ML       | 21-05-24 |
| REV:    | DESCRIPTION:                       | BY:      | DATE:    |
| STATUS: |                                    | PLANNING |          |

|          |                                                                                               |
|----------|-----------------------------------------------------------------------------------------------|
| ADDRESS: | NETLEY & HIGHFIELD CRICKET CLUB<br>VT SPORTS GROUND, PORTSMOUTH ROAD<br>SOUTHAMPTON. SO19 9PW |
|----------|-----------------------------------------------------------------------------------------------|

|                                                      |                   |              |                |
|------------------------------------------------------|-------------------|--------------|----------------|
| SITE: VT SPORTS GROUND,<br>PORTSMOUTH ROAD. SO19 9PW |                   |              |                |
| TITLE: LANDSCAPE & TREE<br>PROTECTION PLAN           |                   |              |                |
| SCALE AT A3:<br>1:500                                | DATE:<br>09-05-24 | DRAWN:<br>ML | CHECKED:       |
| DRAWING NO:<br>24-001-106                            |                   |              | REVISION:<br>A |
