


Report date
February 12th 2024



Assigned to Miller Homes

Pheasant Road
Boorley Gardens
Boorley Green
Hedge End

Site Ref.T17-2

Stage 1 report
Road up to base course tarmac

Verification summary report that T17-2 has
been inspected throughout construction and
in accordance with approved plans

All works carried out to approved drawings
and constructed to HCC specifications

Drawing No. 46130/530

Compiled by

David Wootton

OST Engineering


12.2.2024

Checked by

Stephen Townsend FIHE Cert IOSH MIIRSM

OST Engineering

ostengineering@mail.com

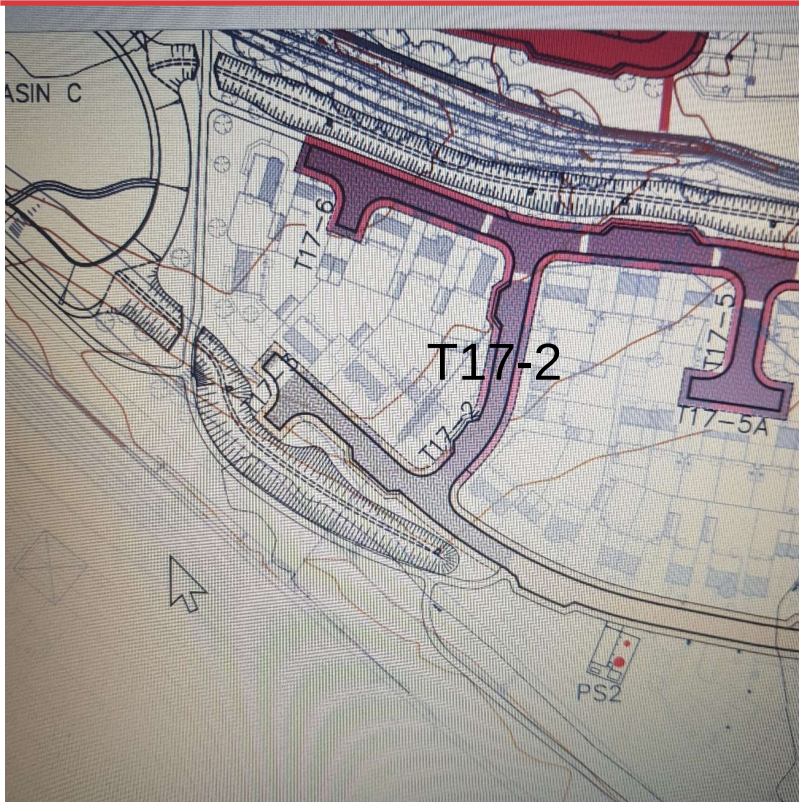

Site location plan of T17-2

Base tarmac finish
To be block paved on completion

Teram laid to compacted sub grade

PC1 and PC3 kerbs as required with ST1 concrete
bed and backing

150mm x 50mm path edgings where required
laid and backed with ST1 grade concrete

150mm 6f5 capping laid and compacted

150mm type 1 stone laid and compacted

90mm AC32 dense base tarmac laid and compacted

80 mm block paving on a 30mm sand bed finish will be recorded
on phase 2 report



T17-2

At its start at T17-4 through to T17 and rumble strips will be added to each end on completion of block paving



T17-2

At 10m and tarmac ramps for access purposes



T17-2

At 20m



T17-3

At 30m



T17-2

At 40m



T17-2

At 50m



T17-2 At its
termination at T17

