


Report date
February 5th 2024



Miller Homes

Stockdove Gardens
Boorley Gardens
Boorley Green
Hedge End

Assigned to Miller Homes

Site reference T17-5 and T17-5a

Stage 2 report
Road complete to block paving finish

Verification summary report that T17-5
and T175 have been inspected throughout
construction and in accordance with
approved plans

All works carried out to approved drawings
and constructed to HCC specifications

Drawing No. 46130/530

Compiled by

David Wootton

OST Engineering

07841 569 236


davidwootton2017@outlook.com

Checked by

Stephen Townsend FIHE Cert IOSH
MIIRSM

OST Engineering

ostengineering@mail.com

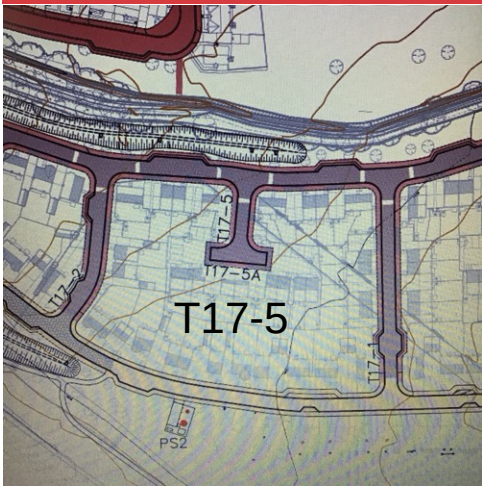

T16-5 site location

BLOCK PAVED FINISHED SURFAC

Teram membrane laid to compacted sub grade

PC1 and PC3 kerbs where required, ST1 concrete bed and backed
150mm x 50mm concrete edgings as and when required

150mm 6f5 capping laid and compacted

150mm Type1 granular sub base compacted in 150mm layers

90mm AC32 HDM base tarmac

30mm graded and compacted sharp sand

80mm Marshall block paving finished with kiln dried brushing in joint sand



Start of T17-5 and a rumble strip will be done at a later date



T17-5
At 10m



T17-5
At 20m



T17-5
At 31m



The point where T17-5a goes left and right



T17-5a left side



T17-5a left side



T17-5a right side



T17-5a right side
