


Report date
February 19th 2024



Stockdove Gardens
Boorley Gardens
Boorley Green
Hedge End

Assigned to Miller Homes

Site Ref T17-4 & T17-4a

Stage 1 report
Road complete to base course tarmac

Verification summary report that T17-4, T17-4a
and T17-6 have been inspected throughout
construction and in accordance with
approved plans

All works carried out to approved drawings
and constructed to HCC specifications

Drawing No.46130/530

Compiled by

David Wootton

OST Engineering


19.2.2024

Checked by

Stephen Townsend FIHE Cert IOSH MIIRSM

OST Engineering

ostengineering@mail.com

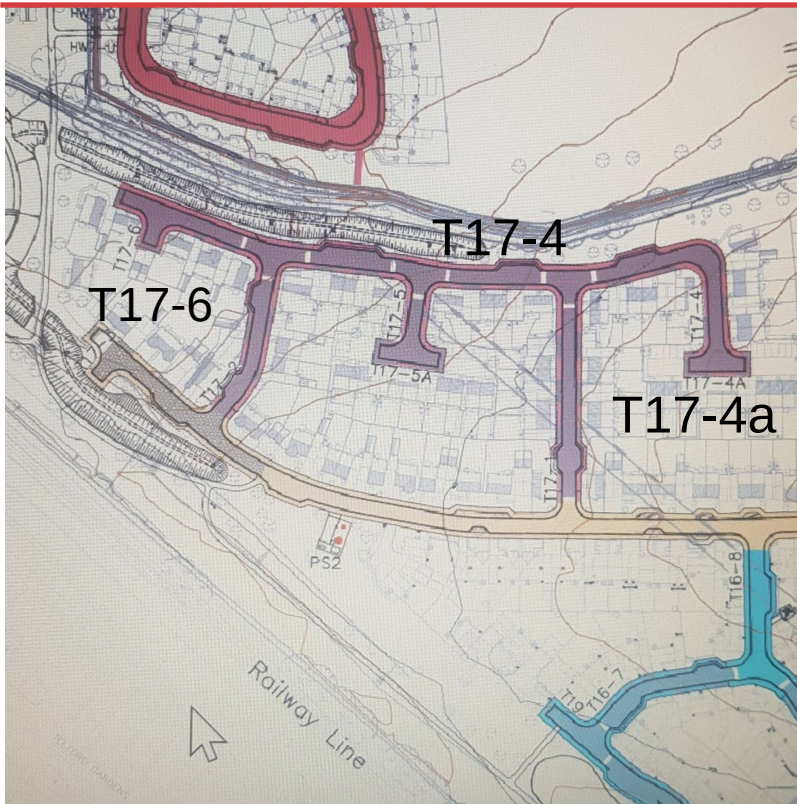

Site location reference

Stage 1 tarmac finished surface

Teram laid to compacted sub grade

PC1 and PC3 kerbs as required with ST1 concrete bed and backing


150mm x 50mm path edgings where required
laid and backed with ST1 grade concrete

150mm 6f2 capping laid and compacted

150mm type 1 stone compacted in 150 layers

90mm AC32 dense base tarmac laid and compacted

This area will be a block paving on a 30mm sand bed finish and
include rumble strips

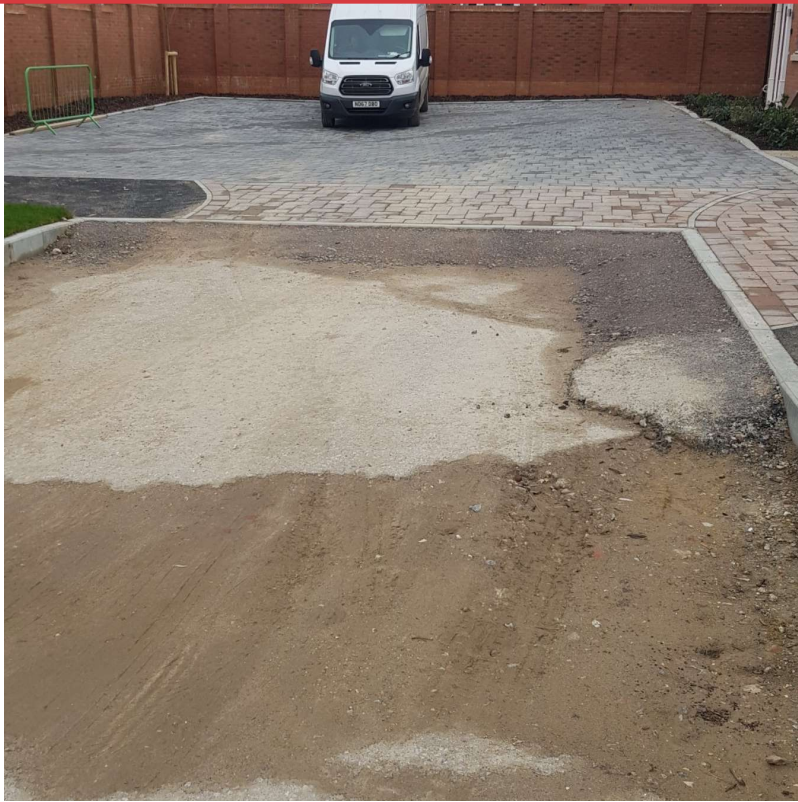

T17-4a

Block paving on both sides
of the Tarmac will be
included on Stage 2 report



Block paving to parking
areas



T17-4
From 0m to 20m



At 40m



T17-4

At 60m



At 80m



At 100m



At 120m



At 140m and a 5m run of
tarmac to meet paving on
T17-5 on the left



At 160m



At 180m



The end of tarmac surface
on T17-4

The block paving to T17-4
and T17-6 will be added to
the Stage 2 report
