


Report date
October 10th 2024



Blackcap Walk
Boorley Gardens
Boorley Green
Hedge End

Assigned to Miller Homes

Site reference T17-1

Stage 2 report
Road complete up to block paving

Verification summary report that T17-1 has
been inspected throughout construction and
in accordance with approved plans

All works carried out to approved drawings
and constructed to HCC specifications

Drawing No. 46130/530

Compiled by

David Wootton

OST Engineering

9.10.2024

Checked by

Stephen Townsend FIHE Cert IOSH
MIIRSM

OST Engineering

ostengineering@mail.com

Formation details

Terram laid to compacted sub grade with 150mm 6f5 capping in 150mm layers and compacted


PC1 and PC3 kerbs as required with ST1 concrete bed and backing

150mm x 50mm path edgings where required laid and backed with ST1 grade concrete

150mm type 1 stone compacted in 150mm layers maximum

90mm AC32 dense base tarmac


80mm block paving laid on a 30mm bed of compacted sand and brushed in with kiln dried jointing sand

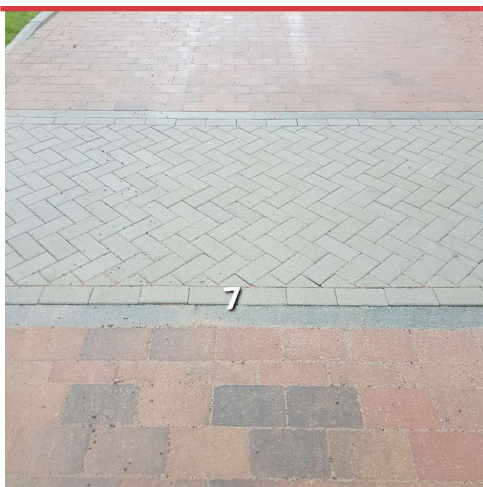


T17-1 at its start on T17-4 and rumble strip has been added



T17-1 at 20m

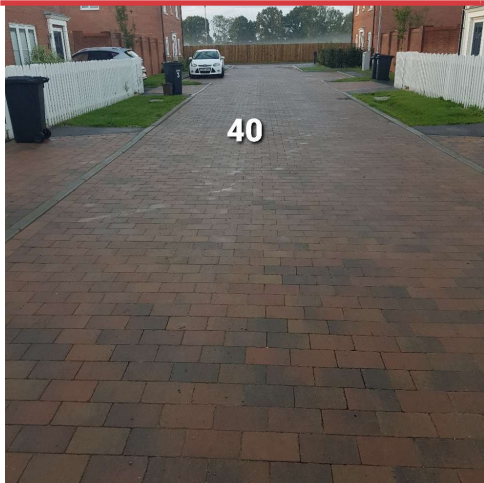

At 40m and showing pull in areas

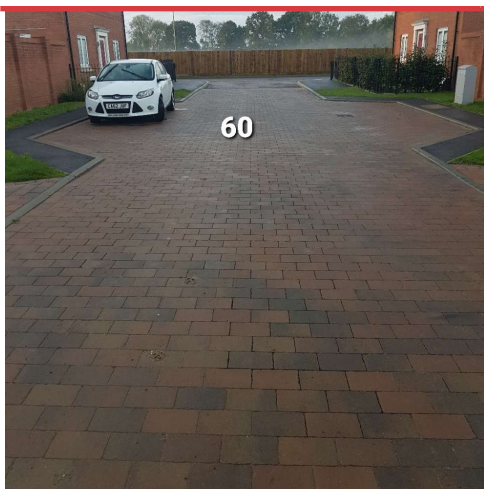

T17-1 at 60m and nearing T17



At 66m and the end rumble strip at T17
