


Report date
October 10th 2024



Pheasant Road
Boorley Gardens
Boorley Green
Hedge End

[Site reference T17-2](#)

Assigned to Miller Homes

Stage 2 report
Road up to block paving completion

Verification summary report that T17-2 has
been inspected throughout construction and
in accordance with approved plans

All works carried out to approved drawings
and constructed to HCC specifications

Drawing No. 46130/530

Compiled by

David Wootton

OST Engineering

9.10.2024

Checked by


Stephen Townsend FIHE Cert IOSH
MIIRSM

OST Engineering

ostengineering@mail.com

Formation details


- *Teram laid to compacted sub grade
- 150mm 6f5 capping in 150mm layers and compacted
- *PC1 and PC3 kerbs as required with ST1 concrete bed and backing
- 150mm x 50mm path edgings where required laid and backed with ST1 grade concrete
- *150mm type 1 stone compacted in 150mm layers maximum
- 90mm AC32 dense base tarmac
- *80mm block paving laid on a compacted bed of sharp sand and finished with kiln dried brushing in joint sand

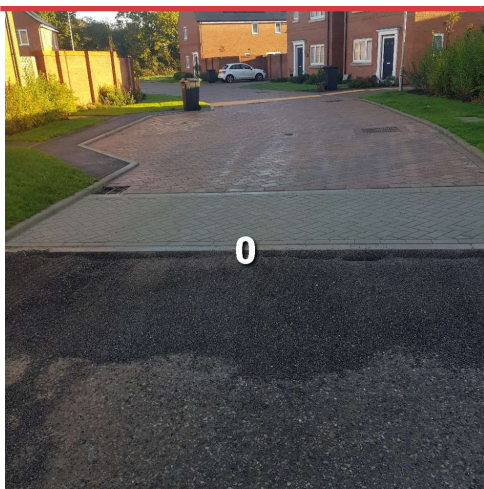


T17-2 and showing the rumble strip at its start at T17



20m in from T17

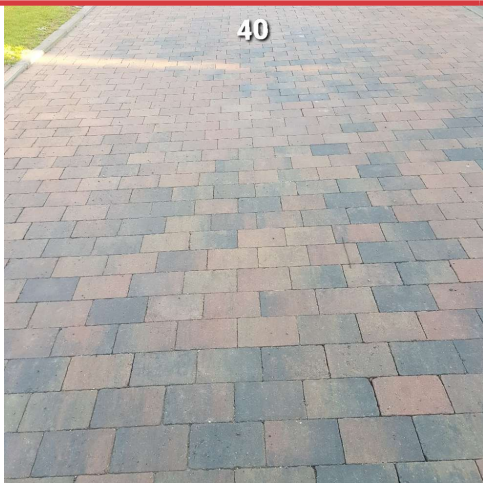

T17-2 at 40m

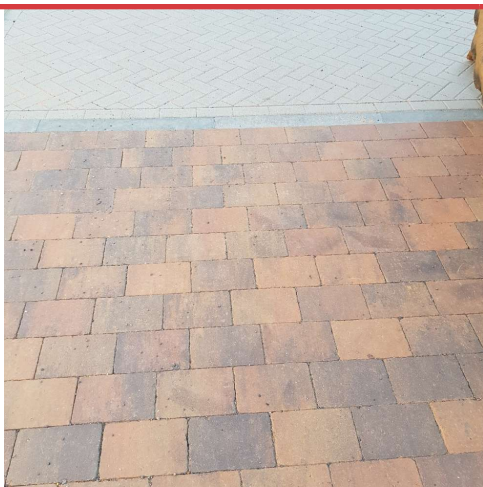

T17-4 and at the rumble strip
as it joins T17-4
