


Report date
October 9th 2024



Stockdove Gardens
Boorley Gardens
Boorley Green
Hedge end

Site reference. T17-4, T17-4a and T17-6

Assigned to Miller Homes

Stage 2 report

Road complete to block paving surface incorporating rumble strips

Verification summary report that T17-4 and T17-4a have been inspected throughout construction and in accordance with approved plans

All works carried out to approved drawings
and constructed to HCC specifications

Drawing No. 46130/530

Compiled by

David Wootton

OST Engineering

9.10.2024

Checked by

Stephen Townsend FIHE Cert IOSH
MIIRSM

OST Engineering

ostengineering@mail.com

Finished road formation

Teram membrane laid to compacted sub grade

PC1 and PC3 kerbs where required, ST1 concrete bed and backed

150mm x 50mm concrete edgings as and when required

ST1 concrete bed and backing to kerbs and edgings

150mm 6f5 capping laid and compacted

150 mm Type1 granular sub base compacted in 150mm layers

90mm AC32 HDM base tarmac

30mm graded and compacted sharp sand


80mm Marshall block paving finished with kiln dried brushing in joint sand



T17-4a into T17-4 and at the 20m mark




T17-4 at 40m

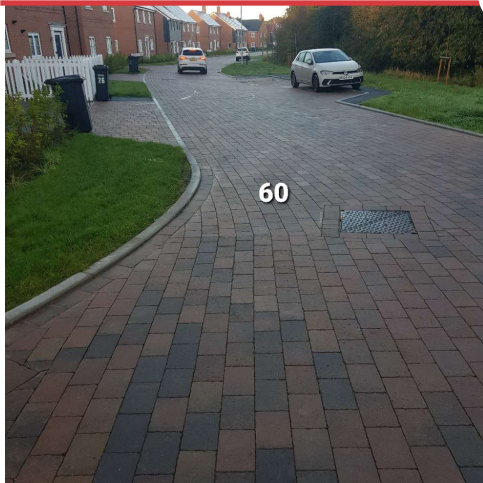

60m in T17-4 and approaching the first rumble strip



T17-4 at 80m and the first of the rumble strips

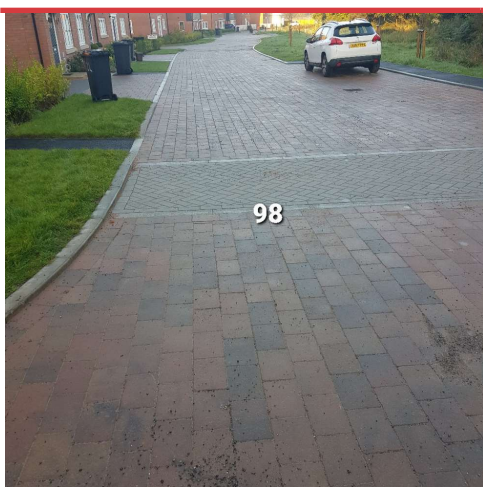

Second rumble strip at 98m



T17-4 at 110m




Third rumble strip at 132m



T17-4 and the fourth rumble strip at 151m




T17-4 at 170m

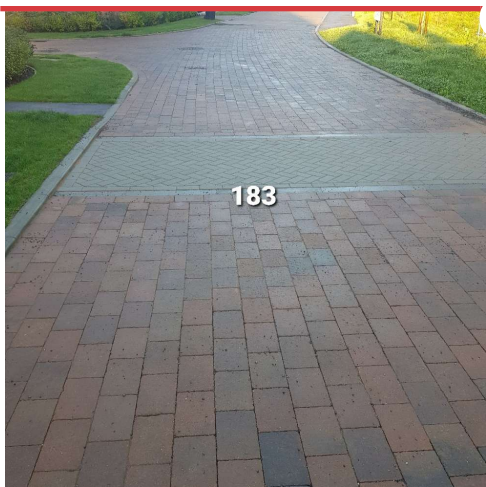

At 183m and rumble strip No. 5



T17-4 rumble strip No. 6 at 208m

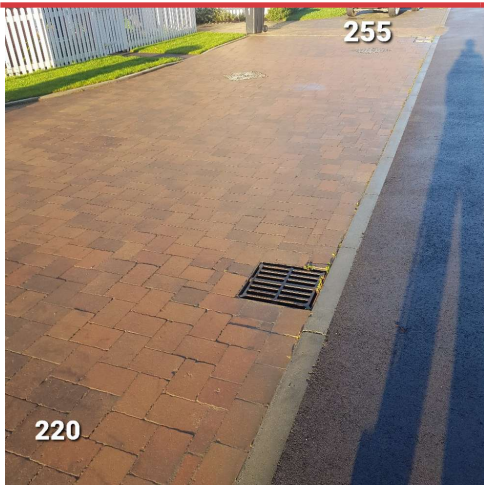

Showing T17-4 at its termination at 255m



An example of the rumble strips on T17-4
