


Report date
February 12th 2024



Assigned to Bellway Homes

House sparrow Way
Boorley Gardens
Boorley Green
Hedge End

Site Ref. T18

Stage 1 report
Road complete to base/binder course

Verification summary report that T18 has been inspected
throughout construction and in accordance with approved
plans

All works carried out to approved drawings
and constructed to HCC specifications

Drawing No. 22-190/014

Compiled by

David Wootton

OST Engineering


12.2.2024

Checked by

Stephen Townsend FIHE Cert IOSH MIIRSM

OST Engineering

ostengineering@mail.com

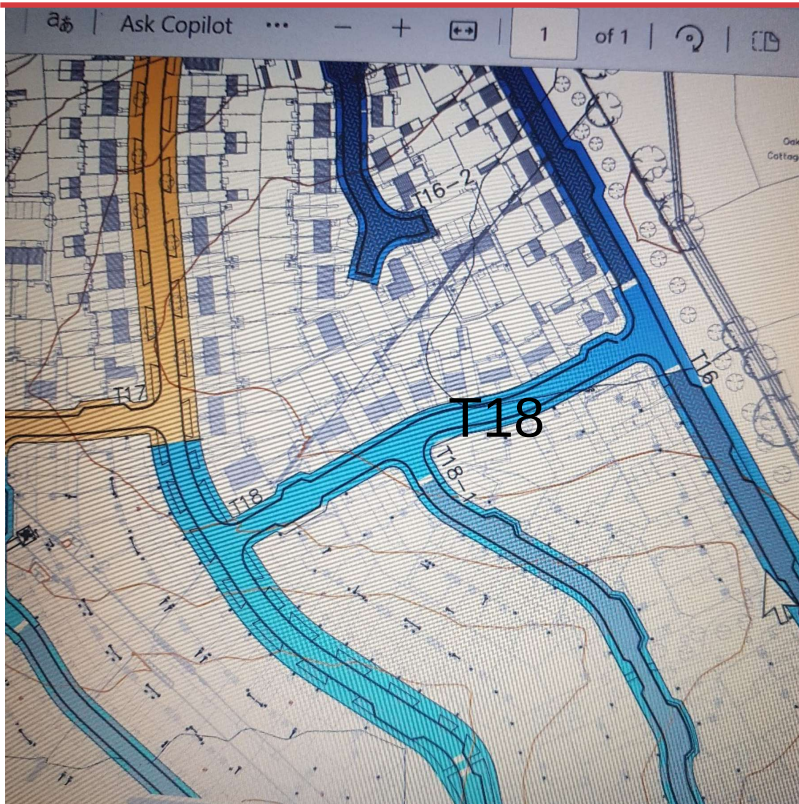

T18

Site location

Tarmac surface specification

Teram laid to compacted sub grade

350mm 6f5 capping in 150mm layers
and compacted

PC1 and PC3 kerbs as required with ST1 concrete bed and backing

150mm x 50mm path edgings where required
laid and backed with ST1 grade concrete

150mm type 1 stone compacted in 150 layers

90mm AC32 dense base tarmac

Wearing course tarmac details will appear on Stage 2 report



1

T18

Start of T18 at its junction
with the secondary route

The following images are at
measured intervals



T18

10 metres



T18

20 metres



T18

30 metres



T18

40 metres



T18

50 metres in and T18-1 goes to the right but is not being constructed at this moment



T18

60 metres and past
T18-1



T18

70 metres in and some
access points have small
sections of tarmac infill for
vehicles



T18

80 metres



T18

90 metres



T18

100 metres



T18

128 metres but carries on
5.5 metres in to T16 to join
up with tarmac between
two block paved areas

