

Tree protection plan
Location of trees, categorisation & protection/management proposals

2, 3, 4, 5, Romsey Close & 2, 4, 6, 8, Toynbee Road,
Eastleigh SO50 9DP

Barrell Plan Ref: 22045-7



barrell
TREE CONSULTANCY

Permission is granted to scale from this drawing for Local Authority Planning Approval purposes relating to tree protection measures only. Where applicable this drawing is to be read in conjunction with the arboricultural report. This drawing is the copyright of Barrell Tree Consultancy 2023 ©

This drawing to be reproduced in colour only.

www.barrelltreecare.co.uk



BS category B Trees of moderate quality



BS category C Trees of low quality



BS category U Trees unsuitable for retention



Trees to be removed



Proposed layout



Estimated tree positions and crown spreads not included on original land survey



Protective barrier/fencing



Construction exclusion zone (CEZ)



Precautionary area where new parking bays will be constructed using a cellular confinement system and a porous wearing course in accordance with the guidance set out in SGN 9.




Root protection area (RPA) boundaries for category B trees



Root protection area (RPA) boundaries for category C trees

Attention LPA Tree Officer - if you would like a 'to scale' printed version of this plan please contact us on 01425 651470 or email 'enquiries@barrelltreecare.co.uk'

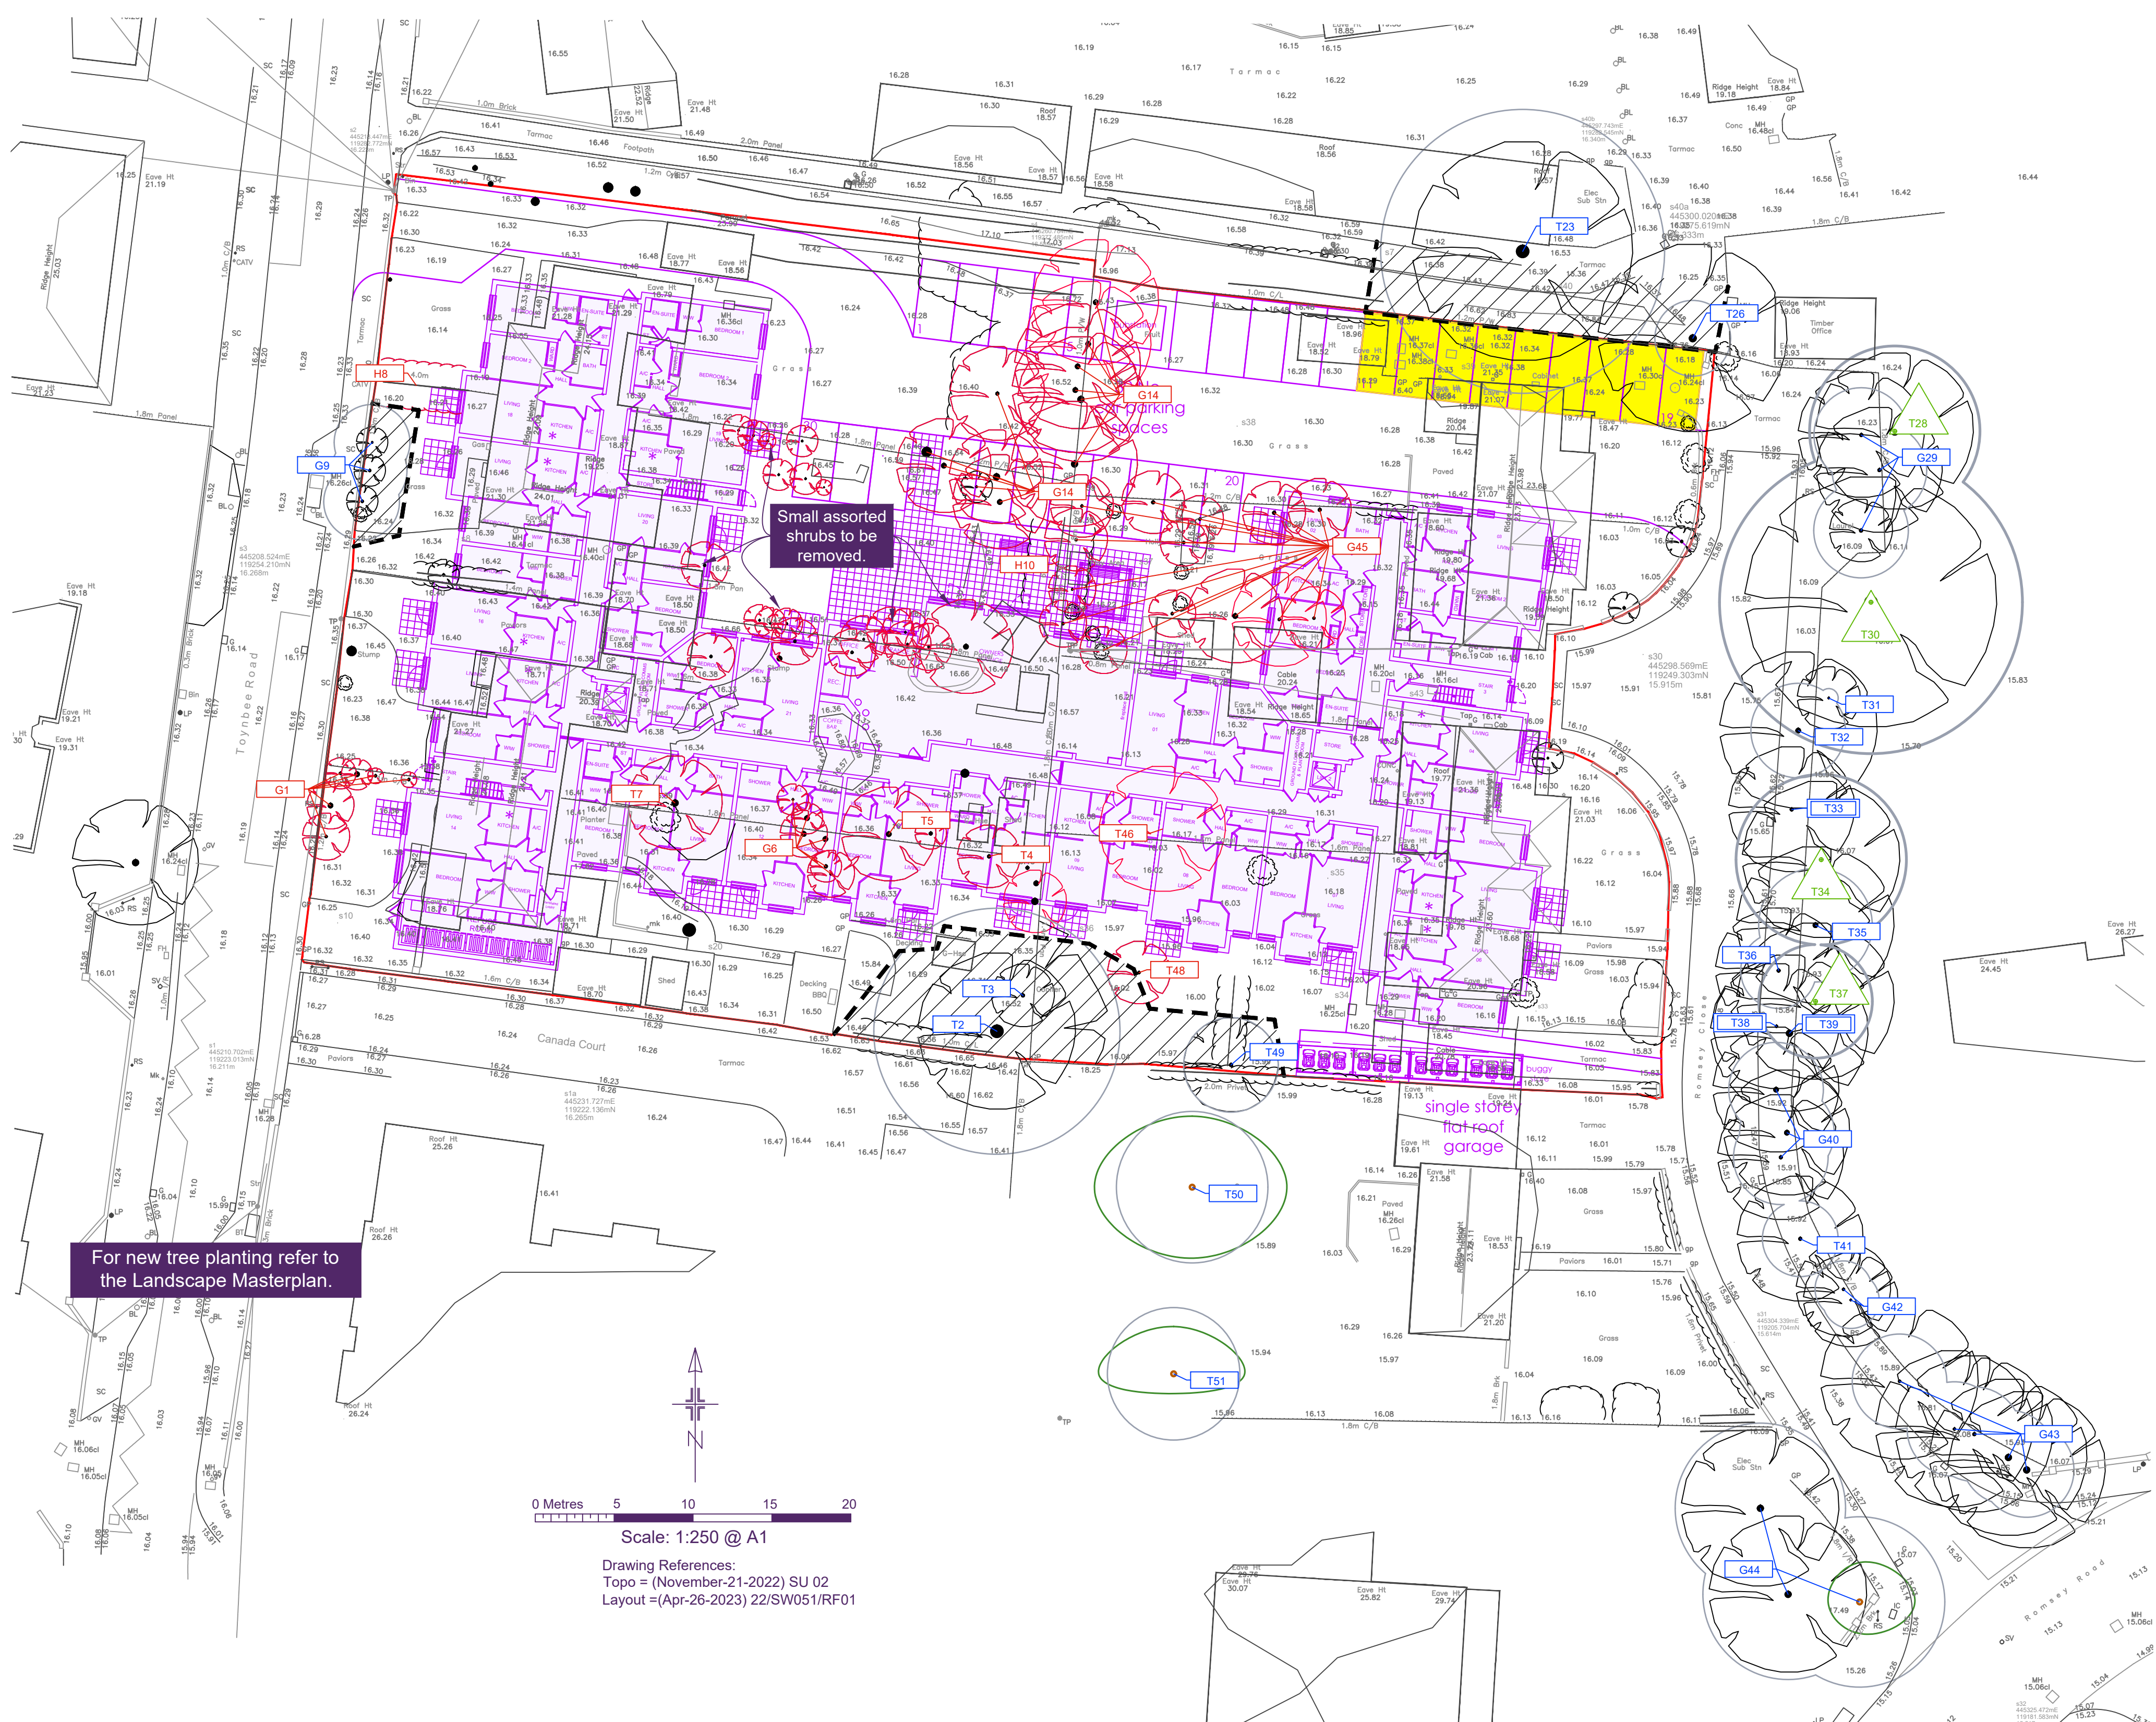

Tree No	Species	Category	RPA Radius	Tree Works
All retained trees & hedges				Carry out safety check and lift over site to 3-4 m as necessary.
G1	Cypress	C	5.4	Fell
T2	Cypress	C	7.8	
T3	Cherry	C	2.4	
T4	Yucca	C	3	Fell
T5	Tree heather	C	3	Fell
G6	Cypress, Holly, Pittosporum	C	5.4	Fell
T7	Pyracantha	C	4.2	Fell
H8	Beech	C	1.2	Fell
G9	Hawthorn, Hazel, Hornbeam	C	2.4	
H10	Cypress	C	3	Fell
G14	Cypress, Magnolia, Privet, Portugal laurel	C	4.2	Fell
T23	Sycamore	C	9	
T26	Sycamore	C	2.4	
T28	Norway spruce	B	5.4	
G29	Sycamore, Plum, Laurel, Laburnum	C	3	
T30	Sycamore	B	9.6	
T31	Birch	C	0.6	
T32	Ash	C	3	
T33	Tree of heaven	U	1.8	
T34	Red oak	B	5.4	
T35	Red oak	C	3.6	
T36	Cherry	C	2.4	
T37	Red oak	B	3.6	
T38	Cherry	U	1.8	
T39	Elm	U	3	
G40	Cherry, Laburnum	C	3	
T41	Cherry	C	2.4	
G42	Plum	C	1.8	
G43	Sycamore, Elm	C	3	
G44	Bay, Laurel, Sycamore	C	5.4	
G45	Holly, Lilac	C	3	Fell
T46	Cypress	C	4.2	Fell
T48	Cherry	C	1.8	Fell
T49	Apple	C	3	
T50	Apple	C	4.8	
T51	Laurel	C	4.2	



SGN 1 *Monitoring tree protection*

Always:

- have a pre-commencement meeting with the tree consultant before development starts
- use the tree consultant to regularly check that protection remains fit for purpose
- use the tree consultant to supervise work in RPAs
- keep a written record of supervision





SGN 2 *Fencing protected trees*

Always:

- install protection before development starts
- make sure protection is fit for purpose, i.e. it prevents damage to trees and soil
- keep protection in place until there is no risk to trees
- get written permission to move or remove any protection





SGN 5 *Site cranes & piling rigs*

Always:

- use the tree consultant to supervise work with cranes and piling rigs in RPAs





SGN 9 *Installing/upgrading surfacing in RPAs*

Always:

- use the tree consultant to supervise work in RPAs
- minimise damage to roots and disturbance to soil in RPAs
- minimise excavation when installing or upgrading surfacing in RPAs






SGN 11 *Installing services in RPAs*

Always:

- use the tree consultant to supervise work in RPAs
- select the least damaging option when installing services, so prioritise trenchless, over broken trench over continuous trench
- hand-dig trenches if trenchless is not feasible

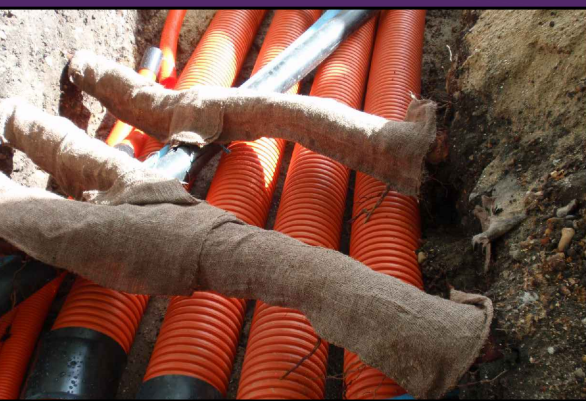




SGN 12 *Landscaping in RPAs*

Always:

- use the tree consultant to supervise work in RPAs
- avoid raising ground levels within 1m of the trunks of retained trees

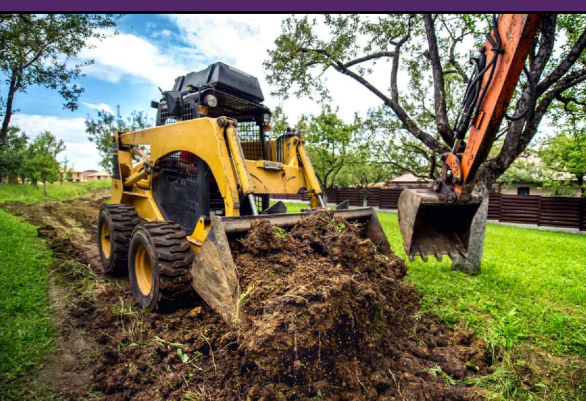

How to use plan

More detailed guidance on each Site Guidance Note (SGN) can be found in a printed hard copy compilation of all the SGNs, **Manual for Managing Trees On Development Sites version 3.1**, issued to the Site Manager at the pre-commencement site meeting (**Note:** This should be retained on site throughout the duration of works). Additionally, an electronic pdf compilation of all the SGNs, was submitted with this drawing to the local planning authority and the client. Alternatively, a pdf of each SGN can be downloaded by:

- clicking the image links in the electronic pdf version of this plan;
- holding a mobile phone QR (Quick Response) code reader over the QR code in the paper version of this plan; or,
- visiting our website at <https://www.barrelltreecare.co.uk/resources/technical-guidance>
