


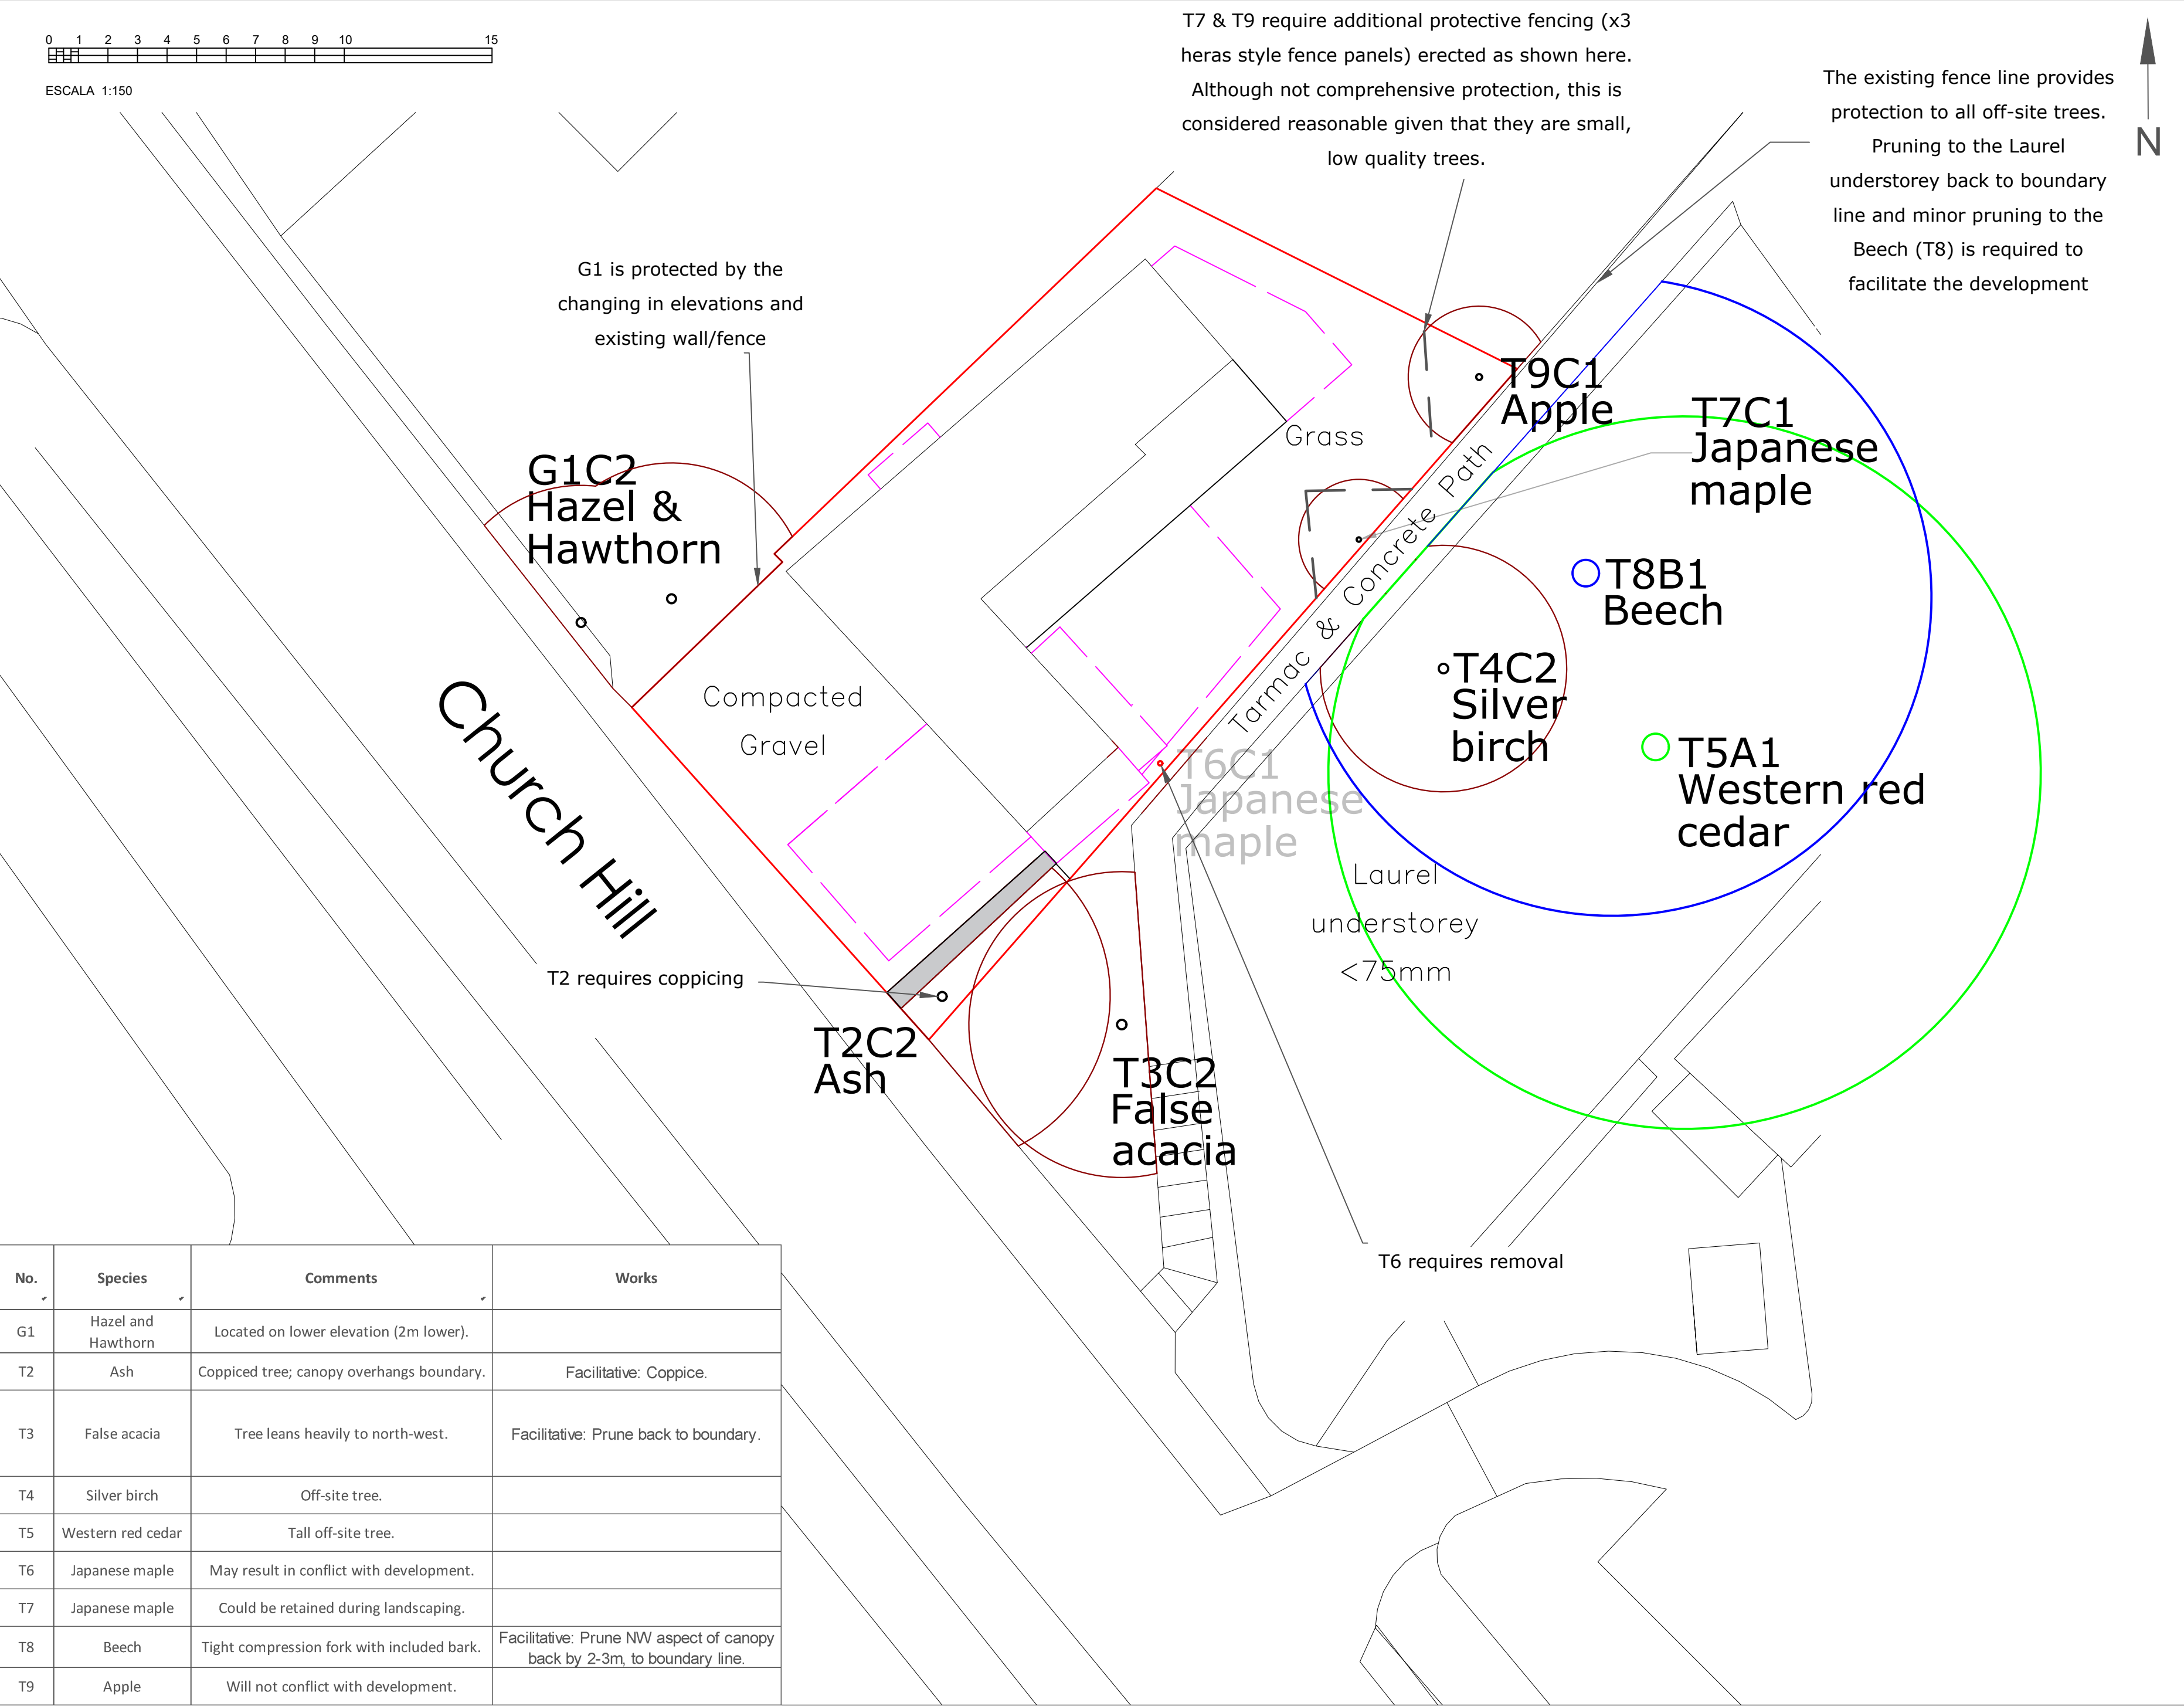

TREE PROTECTION PLAN

CLIENT
Mr & Mrs Jones

SITE ADDRESS
Winston, Church Hill,
West End, Southampton

DRAWING REF
318BV1

SCALE
1:150 @ A2

DRAWING AUTHOR
JA

DATE
Oct 2025

ROOT PROTECTION AREA (RPA)

PROPOSED BUILDING

PROTECTIVE FENCING

Tree Surgery

- Managing encroachment of vegetation over the site is recommended and details are listed in the Tree Schedule within this plan.

Tree Protection

- T8 & T9 are the most important trees in relation to this development. Their RPAs have been amended to reflect the barrier effect the pathway will have on root distribution. Existing fences will protect all off-site trees.
- G1 is located at a lower elevation (approx 2m) from the rest of the site and will also be protected by the existing fence and wall.
- **T7 & T9** are low quality trees located away from the development. Ground protection in addition to the protective fence panels has been considered to "fill in gaps", but deemed unnecessary.

General Construction Management

There must be no changes to soil levels within tree root protection areas. Areas for material storage, site office and worker facilities must be located outside of tree root protection areas. Fires must not be set within the site. Cement mixing must be carried out only where there is no significant risk of contamination of tree root systems. No cement mixing is allowed within 10m of trees to be retained.

- No foundations are proposed.
- Existing services shall be utilised.

This plan is based on the topographical and site layout plans provided. All measurements must be checked with these plans and appropriate documents. Do not scale from drawings, use written dimensions or check on site.

T: 0781747370 E: Ashtonarbor@gmail.com



ASHTON ARBOR
