

East Horton Business Park – Condition 5 – F/23/94668

Please find below the further information requested following the request for further information received for Blocks C & D

Notes -

All Rafts have been installed as per the plans for a ground bearing raft. There are minimal service penetrations for each building, all of which have been surrounded by concrete as well as seal around with the gas membrane.

All rafts have been constructed in accordance with the below detail which was within the verification report.

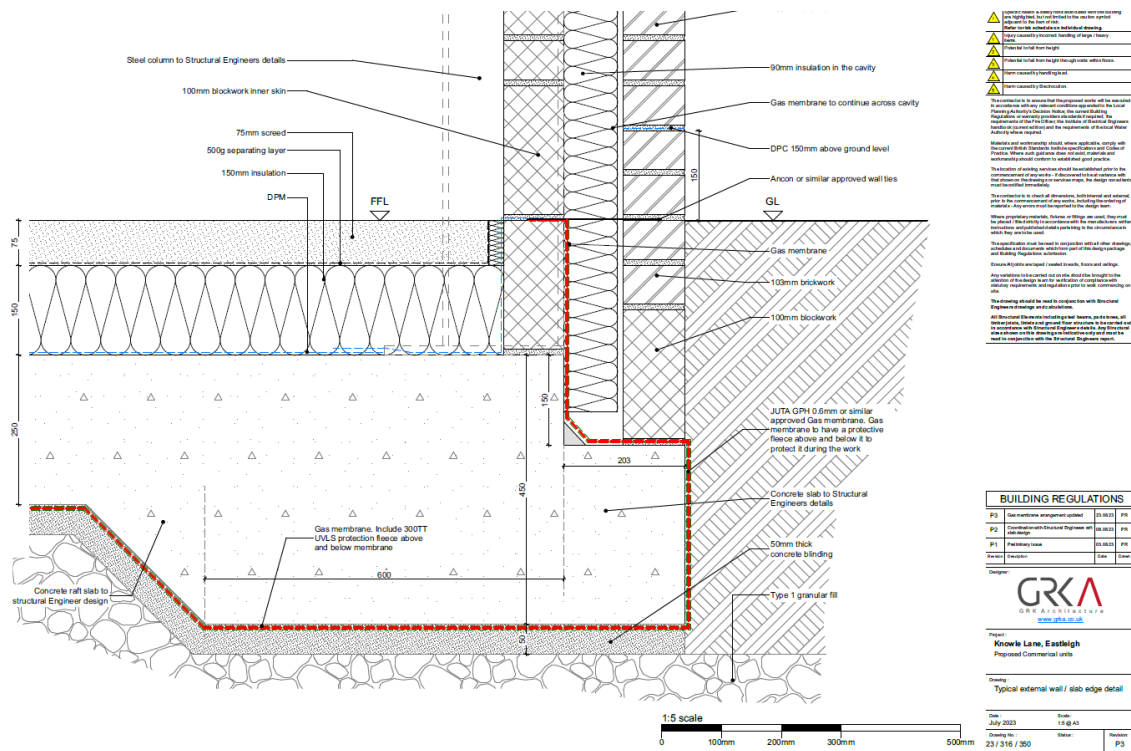


Photo Contents –

- Photo 1 – Block D Slab, showing the full thickness of the slab and 2 service penetrations, fully surrounded by concrete.
- Photo 2 - Block D edge of slab again showing the full depth of 450mm thick concrete raft foundation, and the gas membrane beneath ready to be lapped around the toe.
- Photo 3 - Block C Edge of Slab showing the full depth of the concrete and the gas membrane beneath ready to be lapped around the toe.

Photo 1



Photo 2



Photo 3



Photo 4
