



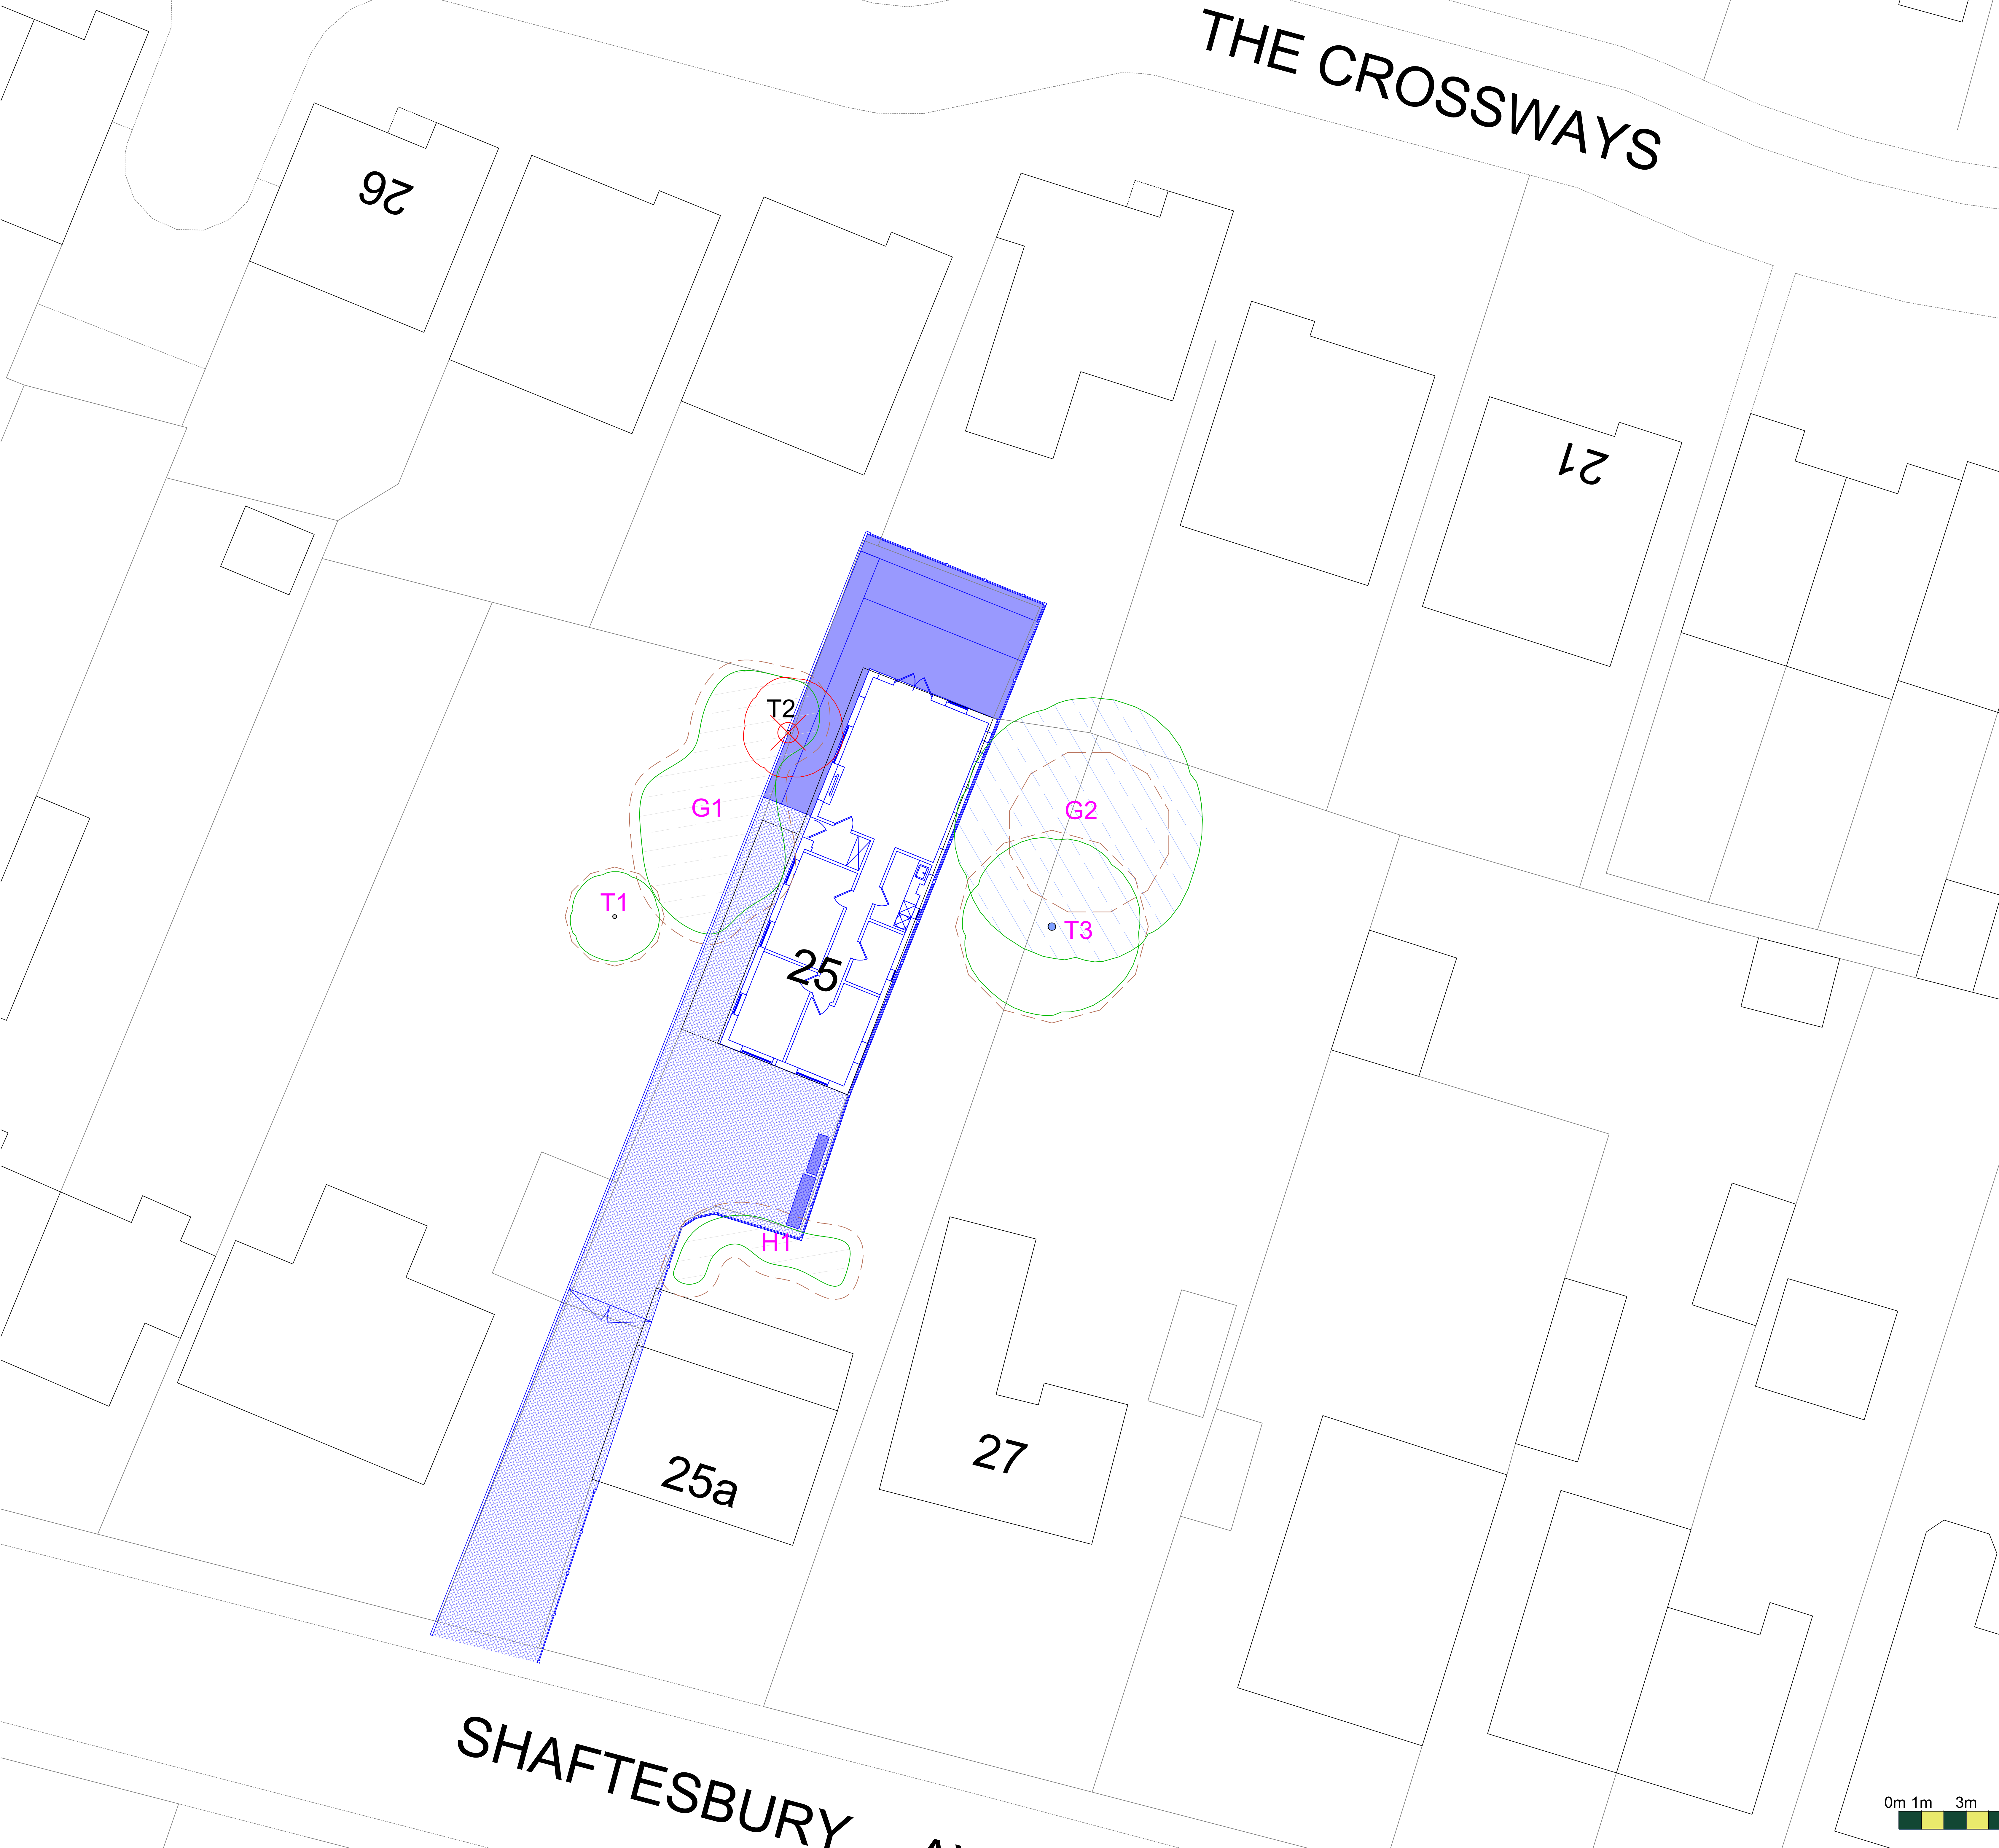

Arboricultural Impacts	
Impacts	Nos. of trees
Trees to be removed	1
Groups / Hedges to be removed (Partial removal of groups)	0 (B)
Trees with proposed incisions into RPA's	0
Groups / Hedges with proposed incisions into RPA's	0
Trees that will require pruning	0
Groups / Hedges that will require pruning	0
Trees to be transplanted	0
Groups / Hedges to be transplanted	0

Tree Work Schedule			
No.	Species	Works	Category
G1	Various	Prune, cut overhanging foliage back to boundary	C2
G2	Common Yew	Prune, cut overhanging foliage back to boundary	B2
H1	Various	Prune, cut overhanging foliage back to boundary	C2
T2	Sycamore	Fell and stump to prevent regeneration	C2

All tree work is to be undertaken in accordance with British Standard BS: 3998:2010 Tree work - Recommendations.
All arising's are to be removed and the site is to be left as found.
Care is to be taken of the ground around retained trees to make sure that it does not become compacted as a result of tree surgery operations. No equipment or vehicles such as timber lorries, tractors, excavators or cranes shall be parked or driven beneath the crowns of any retained trees, to prevent subsequent compaction and root death.

No. of individual trees to be removed			
U	A	B	C
0	0	0	1

No. of groups / hedges to be removed			
U	A	B	C
0 (B)	0 (B)	0 (B)	0 (B)

(-) = Partial removal of a group

Arboricultural Method Statement			
All tree work is to be undertaken in accordance with British Standard BS: 3998:2010 Tree work - Recommendations. Please refer to Arbtech Consulting Ltd. Tree Schedule, Arboricultural Method Statement and Tree Protection Plan, for full details of all surveyed trees and how all aspects of the development may be implemented without detriment to retained trees.			



Unit 3, Well House Barns, Chichester, GU14 0DH
http://arbtech.co.uk, 01243 681170

Project:

25 Shaftesbury Avenue,
Chandlers Ford,
Eastleigh,
SO53 3BR

Client:

RAFAL ZALEWSKI LTD

Drawing:

Arboricultural Impact Assessment

Based on:

241-CFL-00-L-P-100 P02

Drawing No:

Arbtech AIA 01

Date:

Aug 2024

Scale:

1:100 @ A0

Drawn:

CMW

Key:

Tree Nos.:	T1	Tree Categories:	Category 'A' trees	Thunks:	○
RPA's:	○	Category 'B' trees:	●	Category 'B' groups:	○
Category 'C' trees:	○	Category 'C' groups:	○	Trees to be removed:	T2
Existing Site (OD M/s):	○	Proposed Site:	○		

0m 1m 3m 5m 10m
