


Birchen.

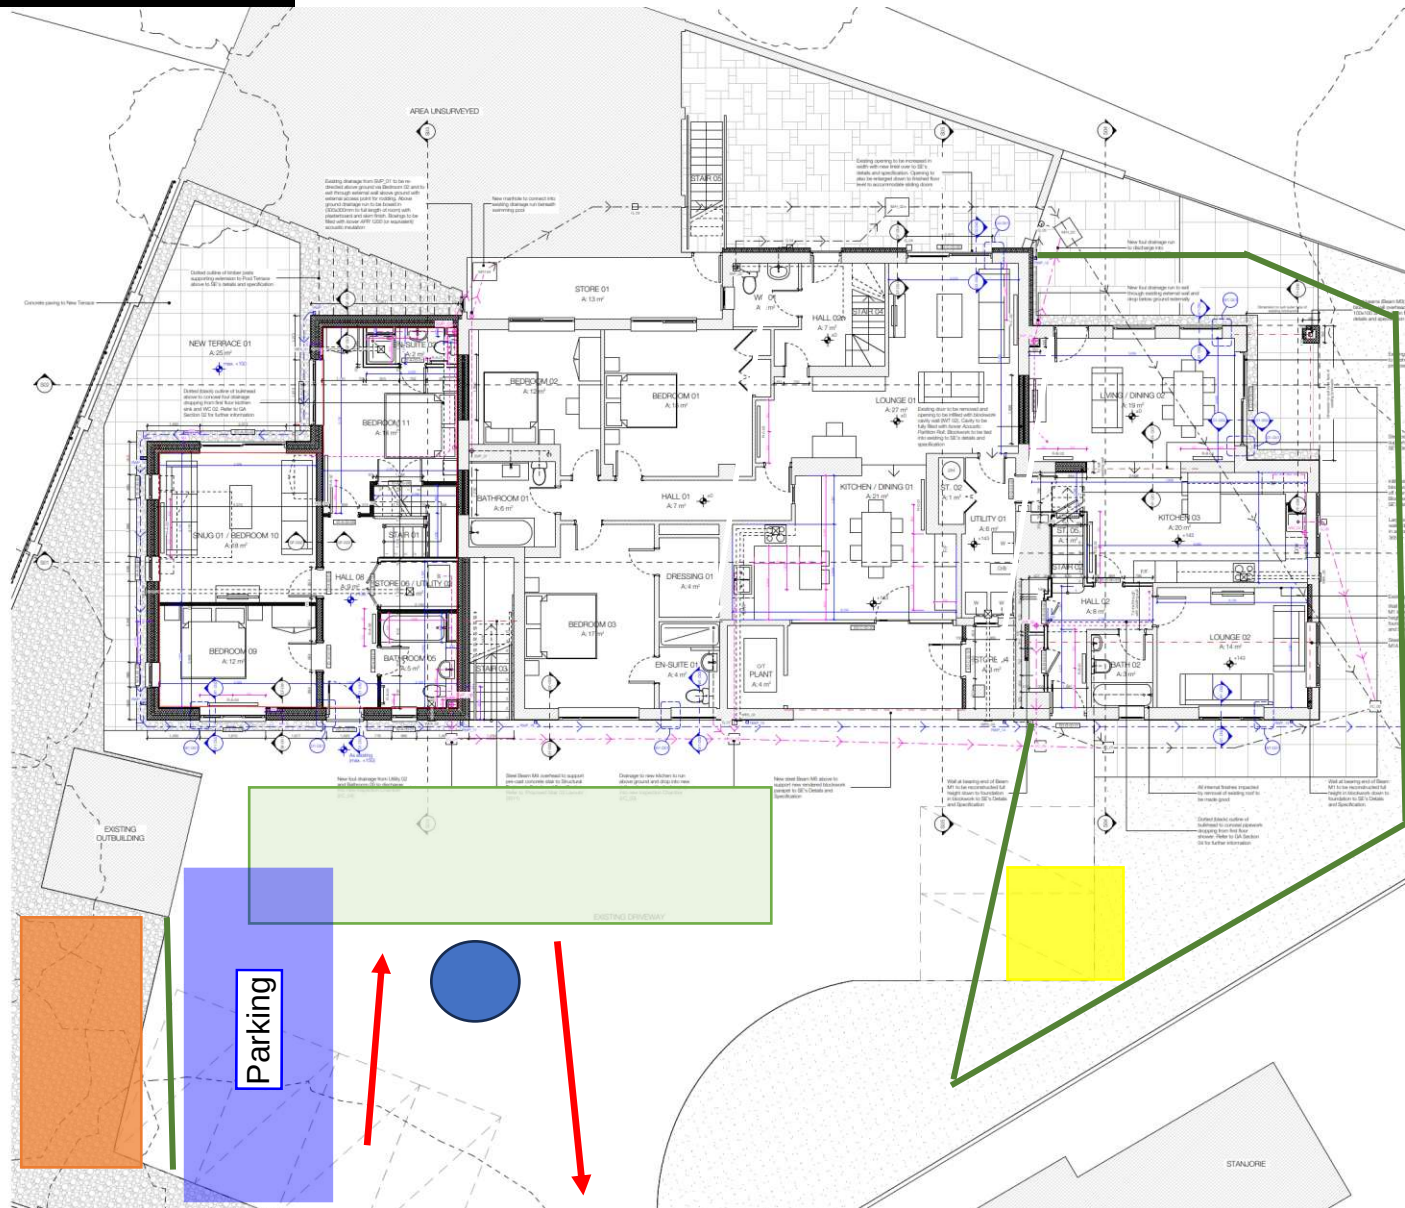

Heras Fencing to be erected to separate site working areas from Brooklands public space. These fences will be move during the rendering phases to ensure work areas are always enclosed.

Lamppost will be removed and roundabout stoned over to improve access and prevent damage. lamppost to be reinstated on project completion.

Area to be used for site office and Welfare

Area to be used for site material storage and skips.

Site deliveries will be banked through the main driveway and be unloaded and materials stored in the appropriate area

Unloading area

The staircase to the front terrace will be demolished during to enable Annexe A to be built. Access to Annexe D will have to be via the rear staircase.

Brooklands, Botley - Site Logistics Plan
