


5.1 Ancillary Products - GRP Dormer

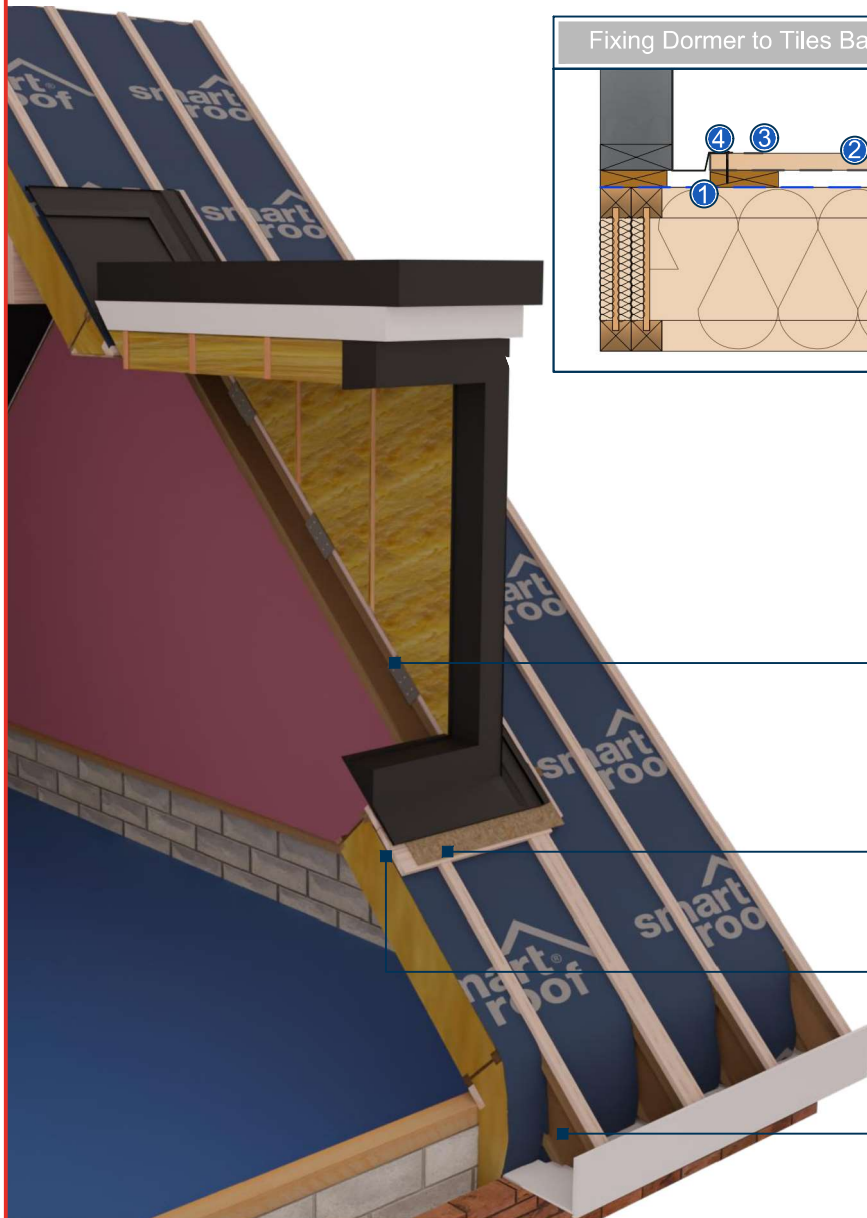

Fixing Dormer to Tiles Batten

1 25x100mm timber board fixed to noggins within Roof Panels

2 Batten fitted by roof tilers. Fixed over tiles membrane and under dormer secret gutter

3 Tiles membrane wrapped around batten and returned under dormer secret gutter

4 Dormer Flange screwed into end of tile batten with self drilling screws with washer

GRP Dormer fixed in place using 6 CAM plates. Plates must be installed at maximum of 300mm from front and rear of the dormer. Each plate fixed with 24no 3.4x35 square twist nails.

9mm OSB strip provisionally fixed for others to trim and secure once tiling gauge is established

22x100mm dormer board at each side and at the top. 2no required at the bottom. Boards to be fixed with 3.1mm x 90mm nails at 200mm centres.

I-Joists rafter

Client Responsibilities:

- ✓ Completing lead work to NHBC standards.
- ✓ Finishing interaction between raked ceiling and dormer horizontal ceiling

